



COMPLETION REPORT PROJECT PD 673/12 REV.1(F)



**“Strengthening the Capacity in
Forest Law Enforcement and
Governance of the Permanent Forest
Estates in Kratie and Mondulkiri
Provinces of Cambodia”**


Prepared by: Eang Savet

07 November 2016, Yokohama, Japan

BACKGROUND OF THE PROJECT

- ✘ The project was approved and financed in November 2012 at the 48th ITTC meeting in Yokohama, Japan. This project was financed by the governments of Japan and Republic of Korea through ITTO.
- ✘ The total budget was US\$ 555,527, which included US \$ 464,033 of ITTO contribution and US\$ 91,494 of the Executive Agency in kind contribution.
- ✘ The project agreement was signed by the Royal Government of Cambodia and ITTO in January 2013.
- ✘ The project was initially planned for 36 months (May 2013-April 2016), a three-months extension (up to July 2016) without additional funding in order to complete execution of the project activities.

PROJECT WORK BREAKDOWN STRUCTURE

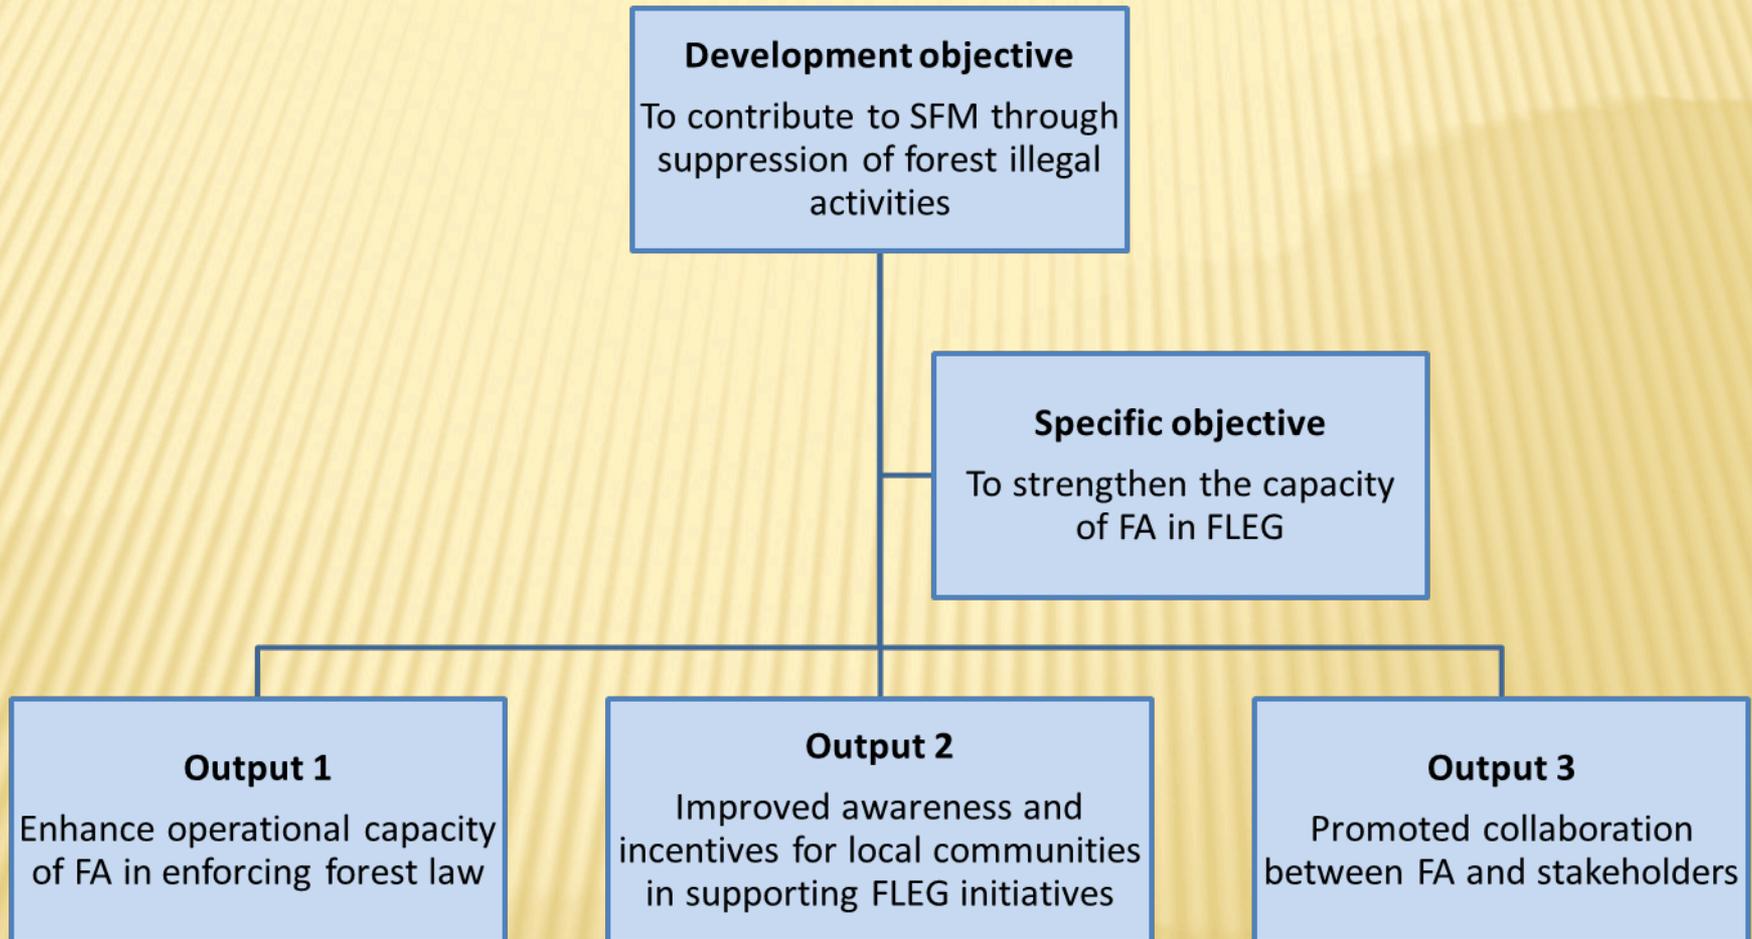

PROJECT OUTCOMES

- ✘ **Output 1:** The well functioning forest crime information system and updated technical guidelines for FLEG operations, procured operational equipment and facilities, FLEG website and project Facebook and disseminated 2013 Booklet on Forest Cover of Kratie and Mondulkiri provinces.



Page	Activity	Insights

A brief of the project

The ITTO project P0673/12 Rev.1 (F) "Strengthening the Capacity in Forest Law Enforcement and Governance of the Permanent Forest Estates in Kratie and Mondulak Provinces of Cambodia" was approved in November 2012 in Yokohama, Japan and funded by the Government of Japan and the Republic of Korea through International Tropical Timber Organization (ITTO).

The project is aimed specifically at strengthening forest law enforcement in the Permanent Forest Estates (PFEs) of Kratie and Mondulak provinces. Its development objective is to contribute to sustainable forest management in Cambodia through suppression of forest illegal activities. The specific objective is to strengthen the capacity of Forestry Administration in forest law enforcement and governance of PFEs of Kratie and Mondulak provinces. The project's expected outputs are: (i) enhanced operational capacity of Forestry Administration in enforcing forest laws in the PFEs of Kratie and Mondulak provinces; (ii) improved awareness and incentive for local communities in respecting forest law enforcement and governance (FLEG) initiatives; and (iii) promoted collaboration between Forestry Administration and stakeholders.

Duration of the project: 36 months
 Starting date of the project: 01 May 2013
 Executing Agency: Forestry Administration of Cambodia
 Address: # 40 Preah Norodom Blvd, Phnom Penh, Cambodia

For more information:
 In-charge name: Dr. Hwan Ok Ma
 Project Coordinator: Forestry Administration
 Division of Forest Management
 International Tropical Timber Organization (ITTO)
 Yokohama, Japan
 Tel: (81-45) 223-1110
 Fax: (81-45) 223-1111
 Email: ma@itto.int



PROJECT OUTCOMES (CONT.,)



- ✘ **OUTPUT 2:** No less than 576 community leaders and members were involved in the different training on techniques relating to livelihood improvement and at least 608 community leaders and members have had their awareness on FLEG and SFM significantly improved.

PROJECT OUTCOMES (CONT.,)

- ✘ **Output 3:** Improved public awareness on FLEG and SFM through wide distribution of thousands of brochure, posters, calendars, comic book etc., enhanced operational capacity of FA in forestry extension operations through implementation of a sound forestry extension program by 58 FA newly trained as extension officers.



CONCLUSIONS

- ✘ The project had been smoothly implemented and successfully achieved its defined outputs and specific objective due mainly to the sound project design, adoption of an appropriate strategy, adequacy of inputs in terms of manpower, funds and time, the generally strong support of the primary beneficiaries and employment of an able Project Monitoring Unit.
- ✘ The primary beneficiaries of the project had demonstrated strong support on project implementation

**THANK YOU VERY MUCH FOR
YOUR ATTENTION**
